



TYPE TEST REPORT

Type test report no. 2600305.01-MHV 21-0009

Type test on a MVS6750-LV High-voltage/Low-voltage Prefabricated Substation

Manufacturer

Sungrow Power Supply Co., LTD.

No. 1699 Xiyou Road, New & High Tech Zone,
Hefei, Anhui, China


TYPE TEST REPORT

OBJECT	MVS6750-LV High-voltage/low-voltage prefabricated substation 30 / 0.8 / 0.8 kV, 6750 kVA, 50 Hz										
CLIENT	Sungrow Power Supply Co., Ltd. Hefei, Anhui Province, China										
MANUFACTURERS	<table><tr><td>High-voltage/low-voltage prefabricated substation</td><td>Sungrow Power Supply Co., Ltd. Hefei, Anhui Province, China</td></tr><tr><td>High-voltage switchgear</td><td>Ormazabal Zhuhai Switchgear Limited. Zhuhai, Guangdong Province, China</td></tr><tr><td>low-voltage switchgear</td><td>Sungrow Power Supply Co., Ltd. Hefei, Anhui Province, China</td></tr><tr><td>Transformer</td><td>Ningbo AUX High technology Co., Ltd. Ningbo, Zhejiang Province, China</td></tr><tr><td>Container</td><td>Singamas Container Industry Co., Ltd. Yixing, Jiangsu Province, China</td></tr></table>	High-voltage/low-voltage prefabricated substation	Sungrow Power Supply Co., Ltd. Hefei, Anhui Province, China	High-voltage switchgear	Ormazabal Zhuhai Switchgear Limited. Zhuhai, Guangdong Province, China	low-voltage switchgear	Sungrow Power Supply Co., Ltd. Hefei, Anhui Province, China	Transformer	Ningbo AUX High technology Co., Ltd. Ningbo, Zhejiang Province, China	Container	Singamas Container Industry Co., Ltd. Yixing, Jiangsu Province, China
High-voltage/low-voltage prefabricated substation	Sungrow Power Supply Co., Ltd. Hefei, Anhui Province, China										
High-voltage switchgear	Ormazabal Zhuhai Switchgear Limited. Zhuhai, Guangdong Province, China										
low-voltage switchgear	Sungrow Power Supply Co., Ltd. Hefei, Anhui Province, China										
Transformer	Ningbo AUX High technology Co., Ltd. Ningbo, Zhejiang Province, China										
Container	Singamas Container Industry Co., Ltd. Yixing, Jiangsu Province, China										
INSPECTED BY	DEKRA Testing and Certification (Shanghai) Ltd. Shanghai, China										
TEST LOCATION	Sate Gird (Changzhou) Electric Power Equipment Quality Inspection and Testing Center No. 218, Donghai Road, Changzhou City, China.										
DATES OF TESTS	20 December 2020 to 15 January 2021										
TEST SPECIFICATION	The tests have been carried out in accordance with IEC 62271-202 (2014), clause 6.2, 6.5, 6.6, 6.7, 6.9, 6.10.2, 6.10.3, 6.10.6, 6.101.3 and annex BB.										
SUMMARY AND CONCLUSION	The prefabricated substation passed the tests.										

This report applies only to the object tested. The responsibility for conformity of any object having the same type references as that tested rests with the manufacturer.

This report consists of 88 pages in total.

DEKRA Certification B.V.



H.L. Schendstok
Certification Manager
Medium & High Voltage Components

Arnhem, 24 February 2021

© DEKRA Certification B.V. All rights reserved

DEKRA Certification B.V. and/or its subsidiaries are not liable for any direct or indirect, incidental or consequential loss originating through or because of the use of the information or data from this document or due to the impossibility of using that information or data.

DEKRA Certification B.V. Meander 1051, 6825 MJ Arnhem P.O. Box 5185, 6802 ED Arnhem, The Netherlands
T +31 88 96 83 000 F +31 88 96 83 100 www.dekra-certification.com Company registration 09085396

Copyright: Only integral reproduction of this report is permitted without written permission from DEKRA. Electronic copies in e.g. PDF-format or scanned version of this report may be available and have the status "for information only". The sealed and bound version of the report is the only valid version.


14 ACOUSTIC SOUND LEVEL

Prefabricated substation serial no. RD18039001

Cooling method: Transformer: ONAN. LV cabinets: Air-cooled. Fans forced.

Sound level		
		No load
Measured current	% In	/
Measured voltage	% Ur	100
Measured points		20
Measured height	m	1.5
Length of prescribed contour	m	17
Distance between prescribed contour and principal radiating surface	m	0.3
Distance of microphones	m	0.85
Measurement surface	m ²	54.33
Within the prefabricated substation		
Average A-weighted background noise pressure level before measurement L_{bgA1}	dB	35.5
Average A-weighted background noise pressure level after measurement L_{bgA2}	dB	35.3
Uncorrected average A-weighted sound pressure level L_{PA0}	dB	41.8
Corrected average A-weighted sound pressure level L_{PA}	dB	40.1
Guaranteed A-weighted sound pressure level L_{PA}	dB	/
A-weighted sound power level L_{WA}	dB	57.9
Guaranteed A-weighted sound power level L_{WA}	dB	/
Transformer only (opened the doors of transformer cabinet)		
Average A-weighted background noise pressure level before measurement L_{bgA1}	dB	38.5
Average A-weighted background noise pressure level after measurement L_{bgA2}	dB	38.5
Uncorrected average A-weighted sound pressure level L_{PA0}	dB	53.0
Corrected average A-weighted sound pressure level L_{PA}	dB	53.0
Guaranteed A-weighted sound pressure level L_{PA}	dB	/
A-weighted sound power level L_{WA}	dB	67.4
Guaranteed A-weighted sound power level L_{WA}	dB	/

Position of microphones during sound level determination

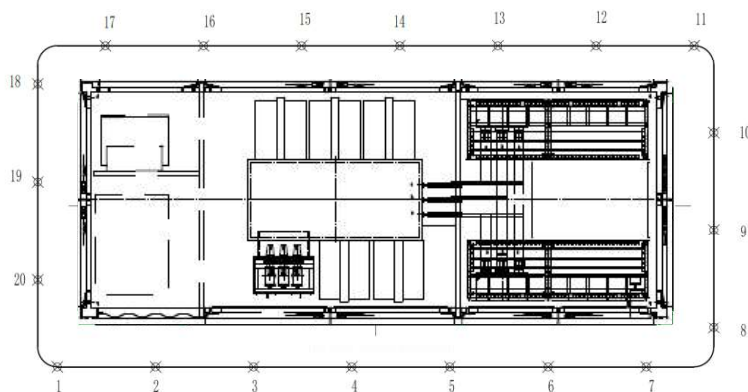

Thermocouple positions in substation
